

Day 1 (8/2/23) Residential DW — COMPLETED

Day 2 (8/3/23) Residential DW — COMPLETED

Petunia Roadways (Red)

Day 4 (8/9/23) Morning Glory Ln. Fingers (Black)

Petunia Roadways (Black)

(8/11/23) Petunia Roadways (Blue)

Morning Glory Ln./ Lily Ct./ Gardenia Dr. Fingers (Yellow)

(8/14/23) Petunia Roadways (Pink)



(8/15/23) Morning Glory Ln. Fingers (Purple)

Petunia Roadways (Yellow)

(8/16/23) Morning Glory Ln./ Gardenia Dr. Fingers (Red)

8/21/23: Petunia Roadways (White)

8/22/23: Petunia Fingers (Green)

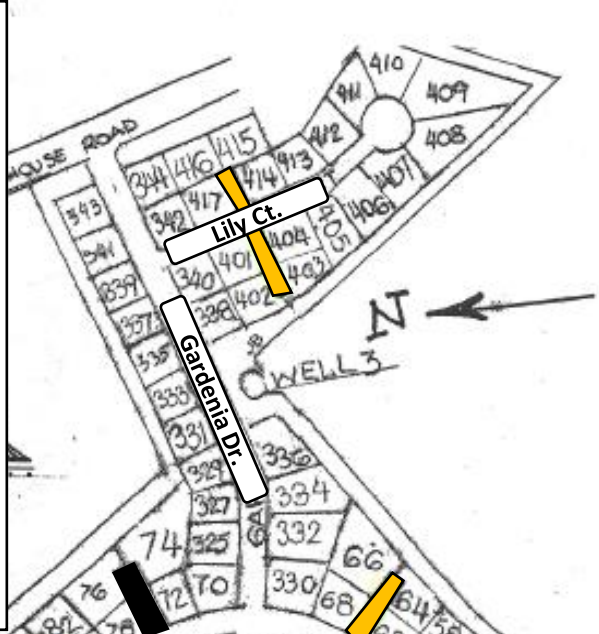

Whiting Station
Community Maintenance
Sealcoat 2023



Important Notes:



▪ When sealcoating work is in your section:

- All vehicles must be out of driveway/finger by 7:00 AM.
- Sealcoat is a liquid and needs up to 24 hours to dry - Do not walk on wet sealer.
- Cars may re-enter the following morning after cones and barricades have been removed.
- Sprinkler systems need to be turned off during sealcoating.
- Be advised tire marks may appear, this is normal, and they will eventually fade away once the sealer cures in 30 days.

▪ Golf Cart Courtesy Shuttle:

During work hours the Eosso golf cart shuttle will be available if you need a ride to and from your car. If you need a ride, call 732-264-7712.

▪ If it rains and work is postponed:

All project dates are weather dependent and subject to change. If it rains on your scheduled date/section, that section will be postponed to the end of the Whiting Station schedule. You will receive a daily notice with your new schedule date, should any dates change.

- If you have any questions, please see Project Manager wearing a Black Vest.

Eosso Brothers Paving thanks you for your cooperation during this project
